


DEVELOPMENT OF EQ 10 BERTH IN INNER HARBOUR OF PORT OF VISAKH

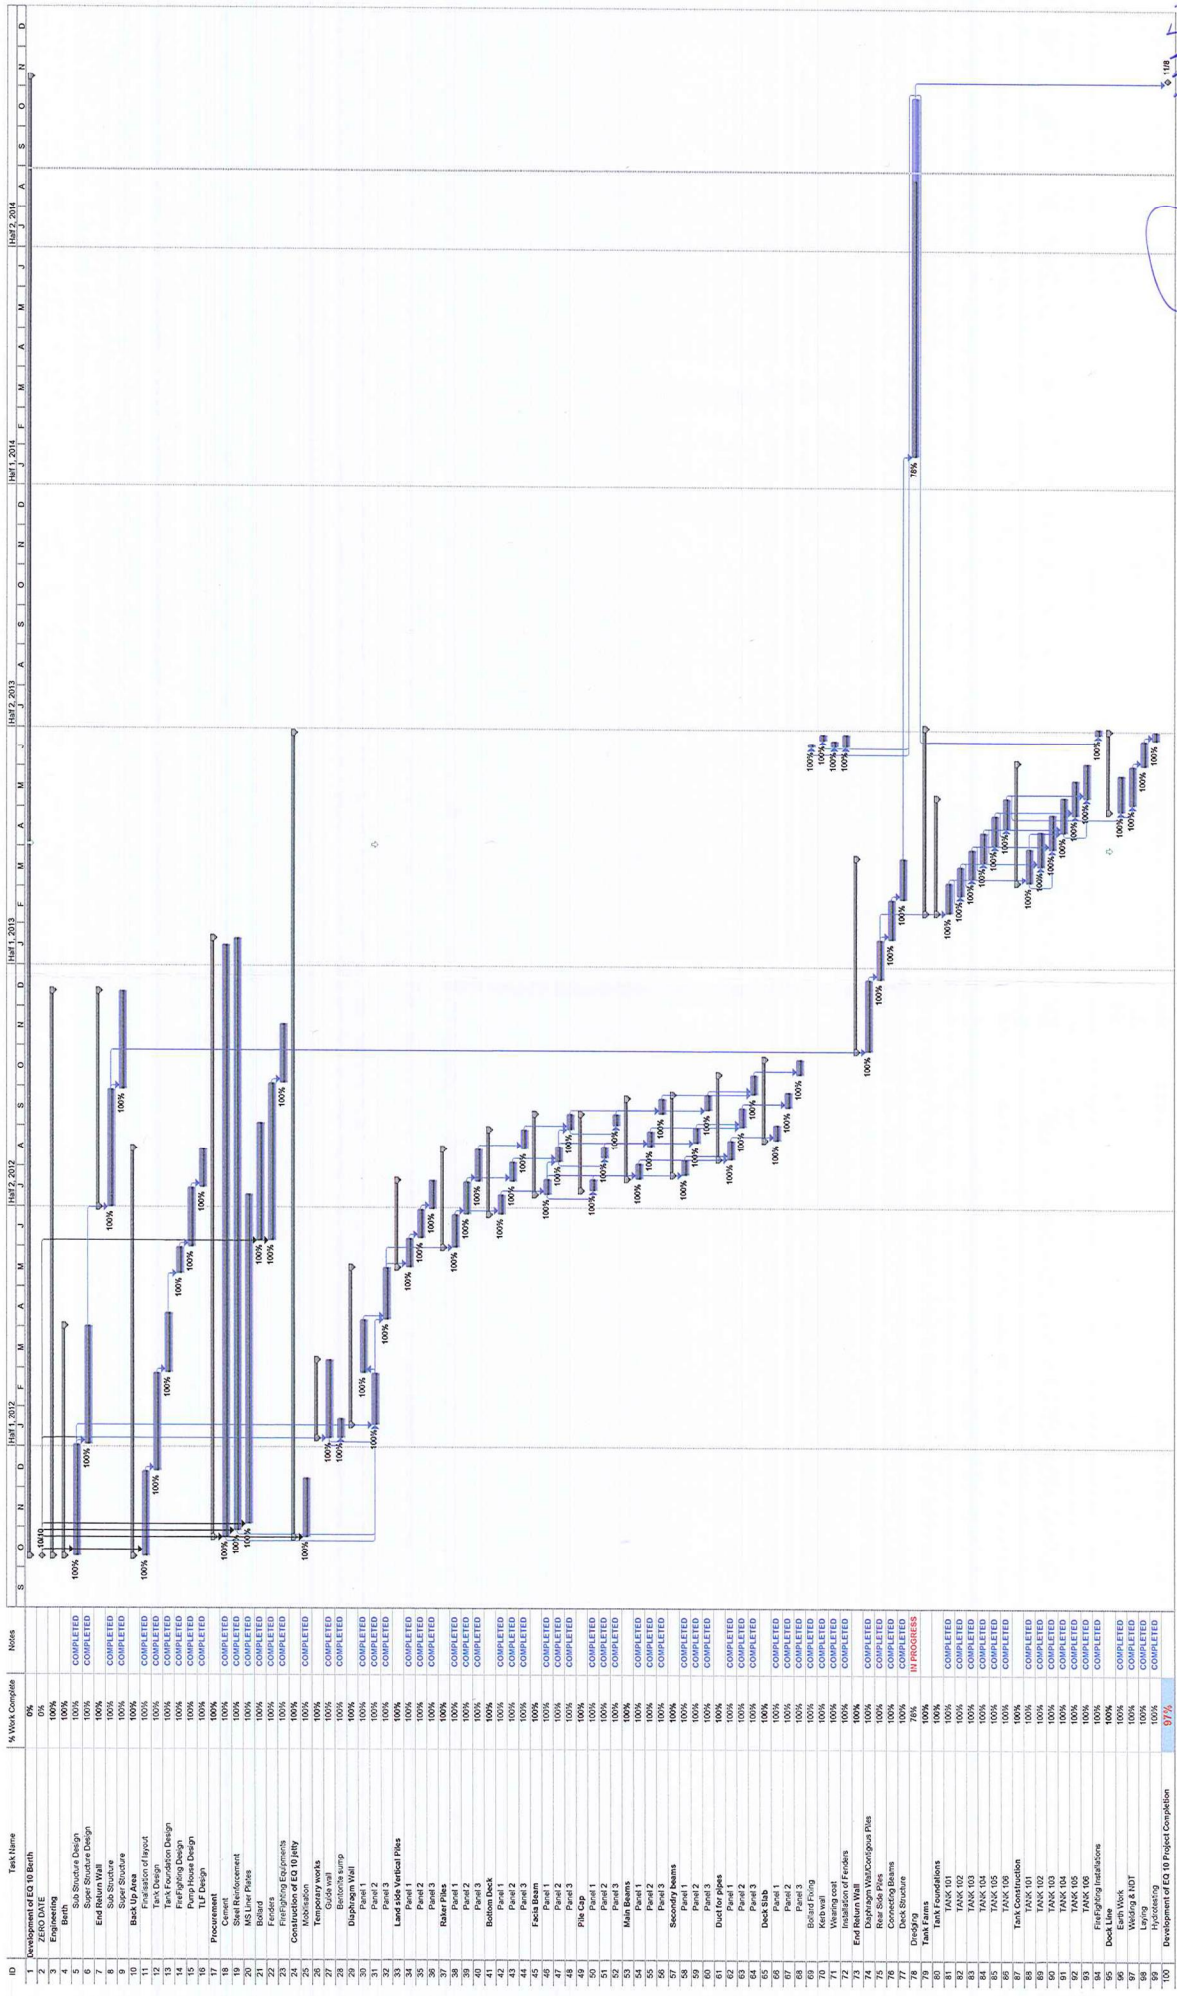

ID	Task Name	% Work Complete	Notes
1	Development of EQ 10 Berth	0%	
2	ZERO DAVE	100%	
3	Earth Retention	100%	
4	Sub Structure Design	100%	COMPLETED
5	Super Structure Design	100%	COMPLETED
6	Sub Structure	100%	COMPLETED
7	Super Structure	100%	COMPLETED
8	Excavation of Foot	100%	COMPLETED
9	Foundation of Foot	100%	COMPLETED
10	Foundation of Foot	100%	COMPLETED
11	Foundation of Foot	100%	COMPLETED
12	Tank Design	100%	COMPLETED
13	Tank Foundation Design	100%	COMPLETED
14	Tank Foundation	100%	COMPLETED
15	Pump House Design	100%	COMPLETED
16	T/LF Design	100%	COMPLETED
17	Phasing	100%	COMPLETED
18	Concrete	100%	COMPLETED
19	Steel Reinforcement	100%	COMPLETED
20	MS Liner Piles	100%	COMPLETED
21	Excavation	100%	COMPLETED
22	Excavation	100%	COMPLETED
23	Excavation	100%	COMPLETED
24	Excavation	100%	COMPLETED
25	Excavation	100%	COMPLETED
26	Excavation	100%	COMPLETED
27	Excavation	100%	COMPLETED
28	Excavation	100%	COMPLETED
29	Excavation	100%	COMPLETED
30	Excavation	100%	COMPLETED
31	Excavation	100%	COMPLETED
32	Excavation	100%	COMPLETED
33	Excavation	100%	COMPLETED
34	Excavation	100%	COMPLETED
35	Excavation	100%	COMPLETED
36	Excavation	100%	COMPLETED
37	Excavation	100%	COMPLETED
38	Excavation	100%	COMPLETED
39	Excavation	100%	COMPLETED
40	Excavation	100%	COMPLETED
41	Excavation	100%	COMPLETED
42	Excavation	100%	COMPLETED
43	Excavation	100%	COMPLETED
44	Excavation	100%	COMPLETED
45	Excavation	100%	COMPLETED
46	Excavation	100%	COMPLETED
47	Excavation	100%	COMPLETED
48	Excavation	100%	COMPLETED
49	Excavation	100%	COMPLETED
50	Excavation	100%	COMPLETED
51	Excavation	100%	COMPLETED
52	Excavation	100%	COMPLETED
53	Excavation	100%	COMPLETED
54	Excavation	100%	COMPLETED
55	Excavation	100%	COMPLETED
56	Excavation	100%	COMPLETED
57	Excavation	100%	COMPLETED
58	Excavation	100%	COMPLETED
59	Excavation	100%	COMPLETED
60	Excavation	100%	COMPLETED
61	Excavation	100%	COMPLETED
62	Excavation	100%	COMPLETED
63	Excavation	100%	COMPLETED
64	Excavation	100%	COMPLETED
65	Excavation	100%	COMPLETED
66	Excavation	100%	COMPLETED
67	Excavation	100%	COMPLETED
68	Excavation	100%	COMPLETED
69	Excavation	100%	COMPLETED
70	Excavation	100%	COMPLETED
71	Excavation	100%	COMPLETED
72	Excavation	100%	COMPLETED
73	Excavation	100%	COMPLETED
74	Excavation	100%	COMPLETED
75	Excavation	100%	COMPLETED
76	Excavation	100%	COMPLETED
77	Excavation	100%	COMPLETED
78	Excavation	100%	COMPLETED
79	Excavation	100%	COMPLETED
80	Excavation	100%	COMPLETED
81	Excavation	100%	COMPLETED
82	Excavation	100%	COMPLETED
83	Excavation	100%	COMPLETED
84	Excavation	100%	COMPLETED
85	Excavation	100%	COMPLETED
86	Excavation	100%	COMPLETED
87	Excavation	100%	COMPLETED
88	Excavation	100%	COMPLETED
89	Excavation	100%	COMPLETED
90	Excavation	100%	COMPLETED
91	Excavation	100%	COMPLETED
92	Excavation	100%	COMPLETED
93	Excavation	100%	COMPLETED
94	Excavation	100%	COMPLETED
95	Excavation	100%	COMPLETED
96	Excavation	100%	COMPLETED
97	Excavation	100%	COMPLETED
98	Excavation	100%	COMPLETED
99	Excavation	100%	COMPLETED
100	Excavation	100%	COMPLETED

Navigation icons: Home, Back, Forward, Print, etc.

Summary: 97% Complete

External Milestones: 100%

External Tasks: 100%

Dashboard
