ASTER INFRATEK PRIVATE LIMITED
CONSTRUCTION SCHEDULE (WQ-8 RE Day to Day Breakup)

L2 Network

ID	Task Name	Duration	Start	Finish
0	**Name of work: Extension of West Quay Return end in replacement of existing RCC Lay by Jetty for coastal cargo and berthing of Harbour crafts and Proposed construction of WQ-8 Return end in the Northern arm**	**117 days**	**Sat 12-07-14**	**Wed 05-11-14**
1	**PART-B:- Proposed construction of WQ-8 Return end in the Northern arm Extension of Inner**	**117 days**	**Sat 12-07-14**	**Wed 05-11-14**
2	**Diapharam walls - Total 16Nos - 12 Nos completed, Balance = 4Nos**	**26 days**	**Fri 26-09-14**	**Tue 21-10-14**
3	Panel No - 28	7 days	Fri 26-09-14	Thu 02-10-14
7	Panel No - 29	7 days	Fri 03-10-14	Thu 09-10-14
11	Panel No - 30	6 days	Fri 10-10-14	Wed 15-10-14
15	Panel No - 31	6 days	Thu 16-10-14	Tue 21-10-14
19				
20	**Pile Muffs - Total 67 nos - 55 Nos completed - Balance=12Nos**	**6 days**	**Sat 27-09-14**	**Thu 02-10-14**
21	Pile Muffs Nos -4	2 days	Sat 27-09-14	Sun 28-09-14
22	Pile Muffs Nos -4	2 days	Mon 29-09-14	Tue 30-09-14
23	Pile Muffs Nos -4	2 days	Wed 01-10-14	Thu 02-10-14
24				
25	**Longitudinal, Main, Copping Beams - Total 52 Nos - 46 Completed, Balance=6nos**	**18 days**	**Sun 28-09-14**	**Wed 15-10-14**
26	Beam no - 27	6 days	Sun 28-09-14	Fri 03-10-14
30	Beam no -28,29	7 days	Thu 02-10-14	Wed 08-10-14
34	Beam no - 30 & 31	6 days	Mon 06-10-14	Sat 11-10-14
38	Beam no 32	4 days	Sun 12-10-14	Wed 15-10-14
42				
43	**Precast slabs - Total-200Nos, 189 Completed, balance= 11Nos**	**5 days**	**Thu 25-09-14**	**Mon 29-09-14**
44	PS1 - 11 Nos	5 days	Thu 25-09-14	Mon 29-09-14
45				
46	**Dredging**	**100 days**	**Sat 12-07-14**	**Sun 19-10-14**
47	**Deck Slab works - 150 Mtrs**	**70 days**	**Wed 20-08-14**	**Tue 28-10-14**
48	**Deck slab -20mtrs**	**13 days**	**Wed 20-08-14**	**Mon 01-09-14**
52	**Deck slab -56mtrs**	**26 days**	**Tue 02-09-14**	**Sat 27-09-14**
56	**Deck slab -30mtrs**	**21 days**	**Sun 28-09-14**	**Sat 18-10-14**
60	**Deck slab -44mtrs**	**19 days**	**Fri 10-10-14**	**Tue 28-10-14**
64	**Wearing coat - PCC 1:1:2**	**8 days**	**Wed 29-10-14**	**Wed 05-11-14**
65	**Paver blocks laying**	**30 days**	**Mon 06-10-14**	**Tue 04-11-14**
66	**Deck Fixtures & Finishing**	**8 days**	**Wed 29-10-14**	**Wed 05-11-14**

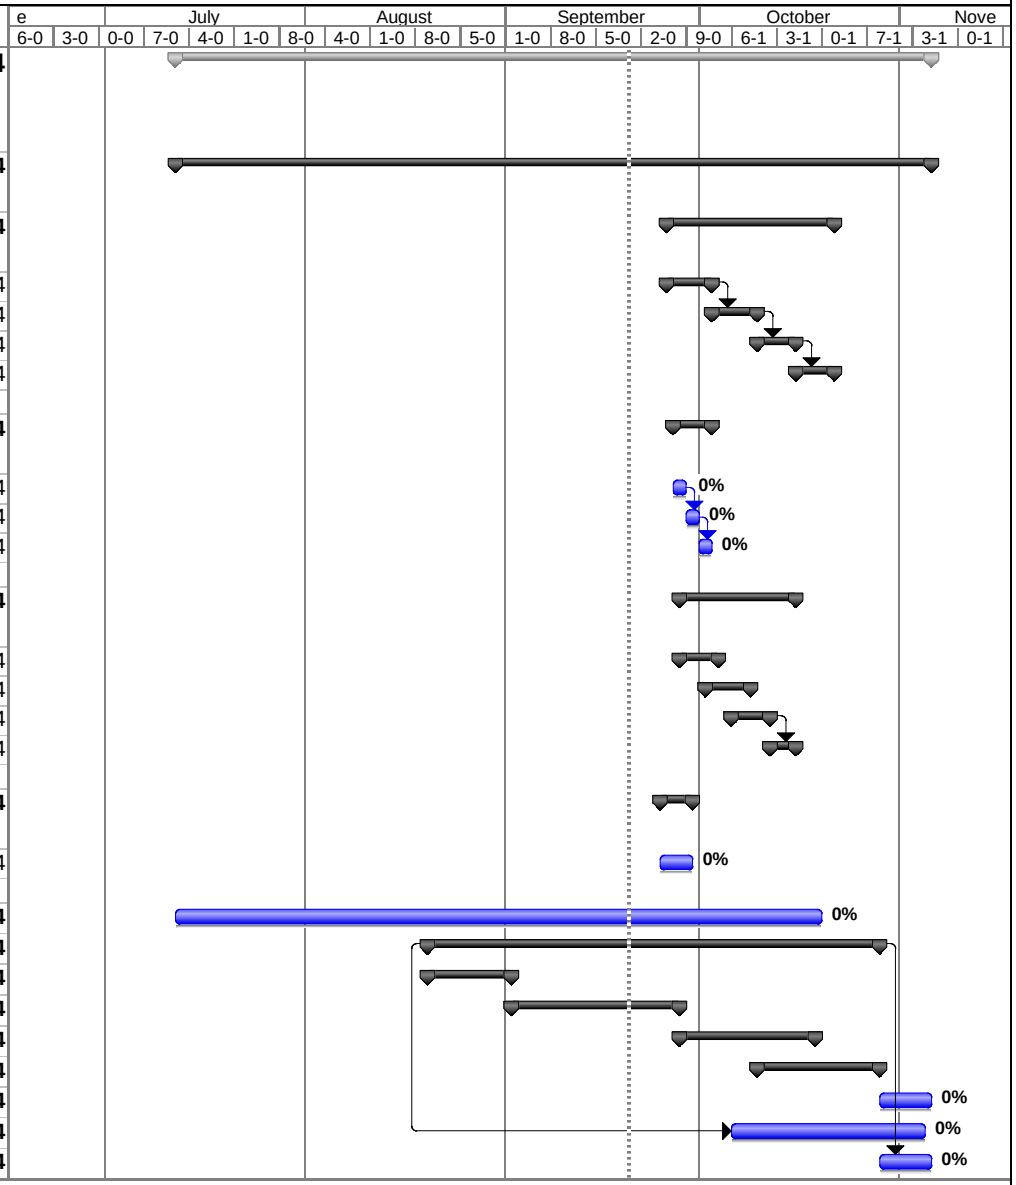

Project: WQ-8 Return End
Date: Sat 20-09-14

Task | Summary | Rolled Up Progress | Project Summary
Progress | Rolled Up Task | Split | Group By Summary
Milestone | Rolled Up Milestone | External Tasks | Deadline
